


THE READINESS FLOW – INDIVIDUAL TRAINING TO MISSION REHEARSAL

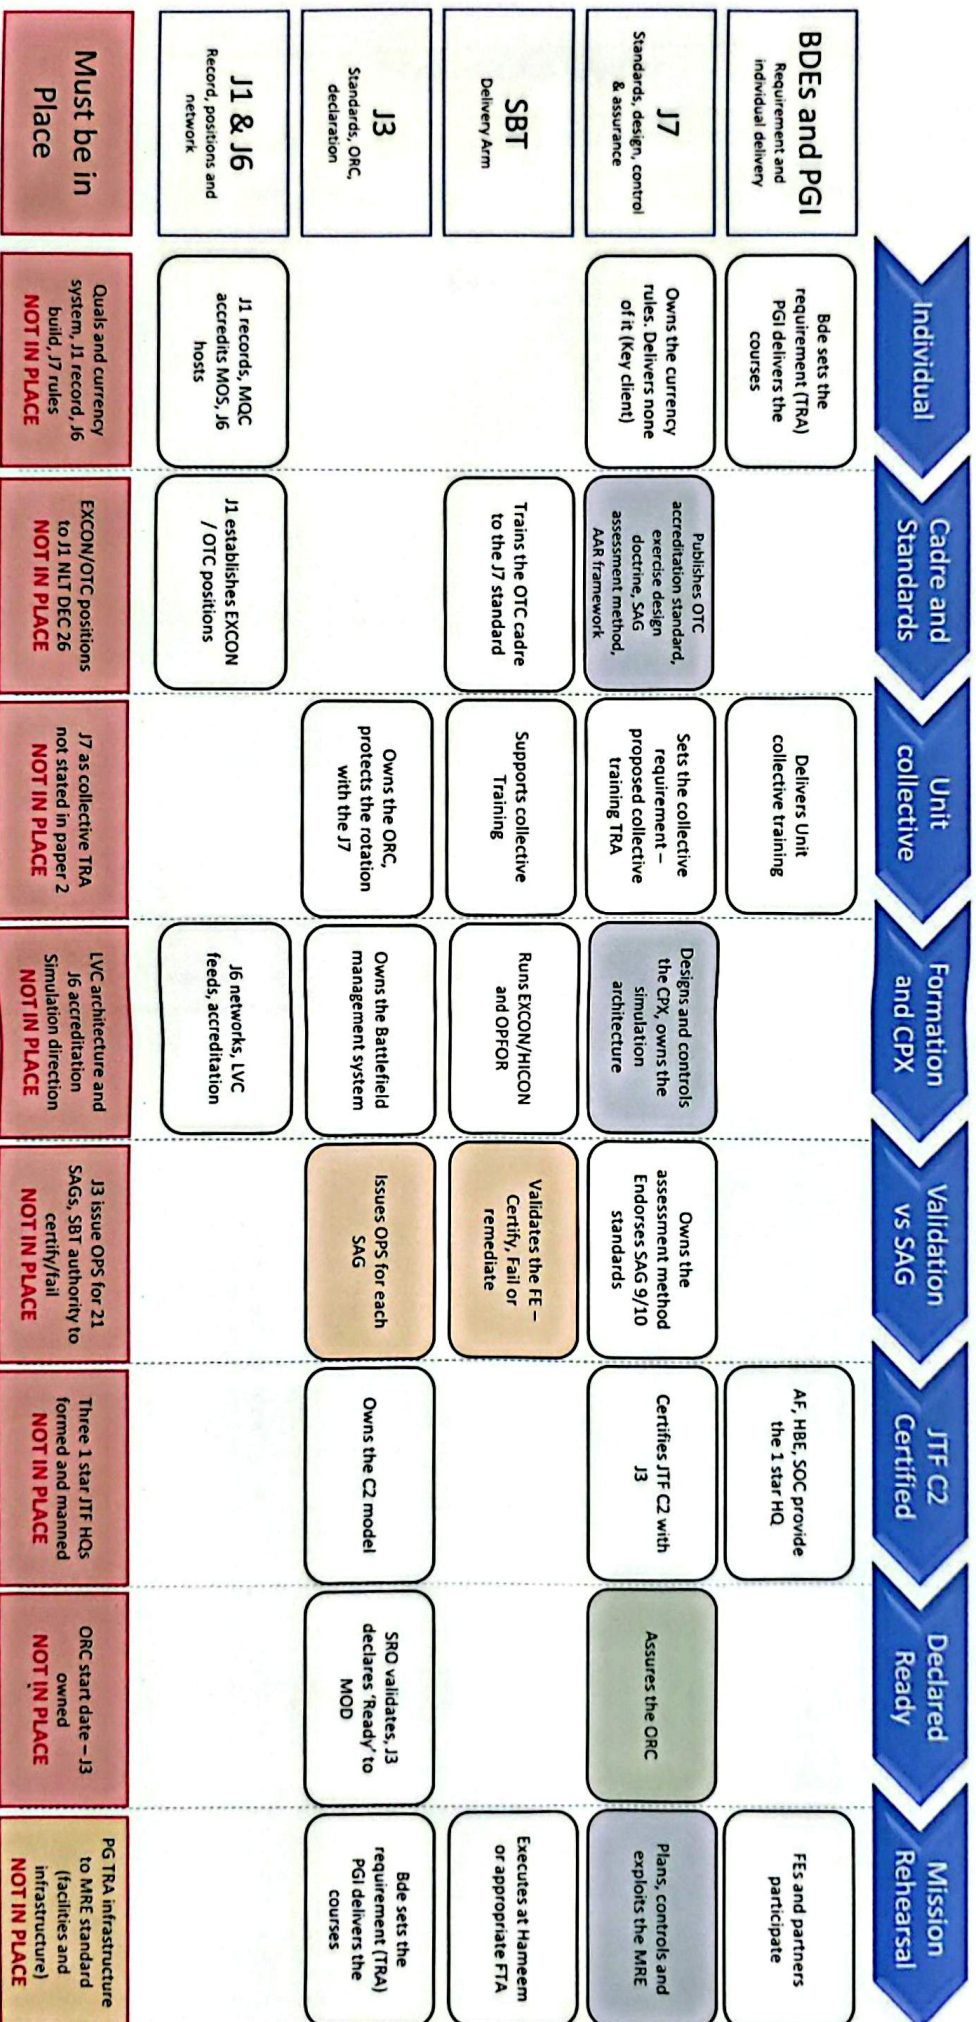

J7 Deliverables Register

Purpose: The Commanders brief sets out what the J7 must achieve and the synchronisation matrix sets out when. This Register sets out what must be written, signed or issued to make those milestones happen
Key: Green = J7 can write and issue on its own authority, Amber = requires another party's approval or input Red = is on critical path or is blocked on an outstanding decision

Ref	Instrument	Deliverable	What it does	Approval	Target	Enables
A - COMMAND, GOVERNANCE AND AUTHORITY						
A1	Staff Paper	J7 Backbrief to Commander PG	Confirms the J7s understanding of Paper 2, declares the FOC horizon for J7 and seeks command concurrence	COMD PG	Aug-26	All subsequent actions
A2	Directive	Convene the J7 Transformation Working Group	Establishes the WG that scopes and drafts the SOP suite, standards and doctrine at section C. Membership, battle rhythm, outputs and reporting line	Comd J7	Aug-26	C1 - C8
A3	Directive	J7 Force generation and Training Directive	The DG-1 governance instrument. Confer's J7 authority over the divisional exercise programme, promulgates the three lines of effort, the critical path & directs Brigade compliance	COMD PG	Jan-27	DG-1
A4	Terms of reference	Force Generation Planning Cell	Establishes the J7/ SBT/J3 governance body, its authority, membership and battle rhythm	COMD PG/J3	Q3-26	B1, DG-1
A5	Submission	J7 Input to the PG 2030 Operations Order	Captures the simulation authority and collective training TRA proposal in the directive	COMD J3	Immediate	E1, A6
A6	Staff Paper	J7 as Collective Training Requirements Authority	Puts the proposal to PG HQ for ruling. Paper 2 names a TRA for individual training only	PG HQ	Q4-26	Stage 3 of readiness flow
A7	Register	J7 Decision, Assumption and Risk Register	Single tracked record of the six open decisions, the ORC assumption and the five program risks. Review at each FGPC	COMD J7	Aug-26	Program control
A8	Directive	J7 Annual Battle Rhythm and Reporting Directive	Sets the planning, synchronisation and reporting cycle J7 runs across the Command and the gate review mechanism	COMD J7	Q4-26	DG-1
B - SBT AND THE FORCE GENERATION PIPELINE						
B1	Terms of reference	Force Generation Pipeline ToR - signature	Recognises SBT as the collective training and validation node under the J7 exercise program. Drafted.	COMD PG/J7/COMD SBT	Q3-26	B2-B6, LoE1
B2	Directive	Recognition and tasking of SBT	Formally directs the relationship the ToR describes - what J7 provides, what SBT delivers and the reporting line into the FGPC	COMD J7	Q3-26	First validation event
B3	Submission	SBT validation authority - request decision	Seeks PG HQ confirmation that SBT may certify, fail and remediate. Without it the chain into the J3's Readiness declaration has no basis	PG HQ	Q4-27	Stage 5 largest single risk
B4	Directive	J7 - SBT resourcing schedule	Commits OPFOR, instrumentation, simulation nodes, an LNO and a quarterly program slot, and the J function support that SBT cannot generate	COMD J7	Q3-26	SBT delivery
B5	Assessment	AAR submission after every assessment	Mandates the return SBT and all exercising units make to the J7 lessons system	COMD J7	Q1-27	F2, F4
B6	Endorsement Paper	SBT SAG9 and SAG 10 assessment standard	J7 review and endorsement of SBTs standards against J3's OPS before first use	COMD J7	Q4-27	First SAG validation
C - STANDARDS, DOCTRINE AND SOPS						
C1	Directive	Standards Working Group - scope and Task	Scopes the SOP suite, sets the drafting program, allocates authors and sets review gates. The authority instrument for C2-C8	COMD J7	Sep-26	C2-C8
C2	Standard	Observer Trainer Accreditation Standard	Defines what an OT must know and demonstrate, and how accreditation is awarded, recorded and renewed. SBT cannot train and grow an OT cadre without it	COMD J7	Q4-26	DG-2/CM1
C3	Doctrine Note	PG Exercise Design Doctrine and Templates	How a PG exercise is scoped, designed, resourced and controlled. Includes MEL/MIL construction and exercise instruction templates	COMD J7	Q4-26	DG-2, DG-4
C4	Method	SAG Assessment method	How J7 benchmarks collective readiness against the OPS J3 issues. J7 owns the method; J3 owns the standards	COMD J7	Q4-26	Stage 5, DG-2
C5	Framework	After Action Review Framework	The single AAR construct used by J7 and SBT alike and the format of the return at B5	COMD J7	Q4-26	F2, LoE3
C6	SOP suite	Individual Training SOP Baseline	The first SOP tranche - individual and cadre level procedures, precedes the collective baseline	COMD J7	Q2-27	SG-2/CM1
C7	SOP suite	Collective and MRE SOP baseline	The second tranche - collective, formation and MRE procedures and exercise C2 structure	COMD J7	Jan-28	DG-3
C8	Standard	Exercise Control (EXCON) Standard	EXCON and HICON structures, appointments, battlerhythm and adjudication rules	COMD J7	Q2-27	DG-3, DG-4
C9	Policy	Exercise Safety and Risk Policy	Risk-to-life governance, safety appointments and the ALARP construct against all J7 directed activities	COMD J7	Q2-27	All live activities
D - THE EXERCISE PROGRAM						
D1	Plan	PG annual Collective Traingning and Exercise Program	The rolling annual program validating each Brigades 2030 tasks against OPS for each SAG. First edition covers 2027	COMD PG/J7	Q1-27	DG-1
D2	Directive	Annual Exercise Program Direction	The tasking instrument issued to Brigades and SBT each year against D1 - participation, resourcing and reporting	COMD J7	Annual from 27	D1 Execution
D3	Directive	Protection of Bde ORC Train/Assure Window	Issued jointly with J3. Protects an FE from all other tasking once it enters Train/Assure	COMD PG/J3	Q1-27	Stage 3
D4	Plan	CPX design and control plan	The design, EXCON structure and control plan for the first J7 run Command Post Exercise	COMD J7	Q4-27	DG-4, CM2
D5	CONEMP	Mission Rehearsal Exercise CONEMP	How the MRE is conceived, scaled, resourced and exploited - the master concept for the 2030 event and its successors	COMD PG/J7	Q2-28	J7 FOC, MRE 2030
D6	Plan	JTF C2 certification plan	How the three 1 star deployable JTF HQs are assessed and certified with J3	COMD J7/J3	Q2-28	DG-5
E - SIMULATION AND SYNTHETIC ENVIRONMENT						
E1	Directive	J7 as Div sim authority	The written capture of COMD J3's verbal direction extending paper 2 task. Recommended veh is the Operations Orders (OPORD)	COMD PG/J3	Immediate	LoE2 entire
E2	CONEMP	PG Live, Virtual Constructive training model	How PG uses simulation before committing resources to live training	COMD PG/J7	Q3-27	DG-6
E3	Specification	LVC architecture and integration specification	The technical statement of requirement issued to J6 and to the force development counter party	COMD J7	Q3-27	DG-6/CM3
E4	Standard	Simulation Integration Standard	What every unit including SBT's EXCON and HICON must comply with to integrate into the DIV architecture	COMD J7	Q4-27	DG-6
E5	Directive	Simulation Boundary	Deconflicts J7's architecture against SBT, J8 Innovation command and Falcon Bde	COMD J7	Q1-27	E1 durability
E6	Specification	Exercise Management software requirement	Statement of Requirements and procurement case. Funding decisions sit at DG-0	COMD J7/J4	Q4-26	DG-0
E7	Standard	Exercise data and instrumentation standard	What is captured in what form. Supplied to innovation command for the PG data capture facility	COMD J7	Q2-27	E3, J8 (IC)

Purpose: The Commanders brief sets out what the J7 must achieve and the synchronisation matrix sets out when. This Register sets out what must be written, signed or issued to make those milestones happen
 Key: Green = J7 can write and issue on its own authority, Amber = requires another party's approval or input Red = is on critical path or is blocked on an outstanding decision

Ref	Instrument	Deliverable	What it does	Approval	Target	Enables
F - TRAINING LESSONS AND OPERATIONAL EXPLOITATION						
F1	Directive	Establish the J7 Training Lessons Cell	Stands up the cell, its establishment, authority to task returns and its reporting line	COMD J7	Q1-27	LoE3
F2	Policy	Training Lessons (OPEX) Policy	Terminology, submission obligations, exploitation route into capability development and force design, bounded to the training half	COMD J7	Q1-27	ST3
F3	Directive	J7-J3 OPEX interface Directive	Names J3 as owner of operational half and sets the two way flow between the systems	COMD J7/J3	Q1-27	ST3, C4
F4	Specification	Lessons Database and Aar return schema	The requirement passed to J6 for hosting and the return format at B5	COMD J7/J6	Q1-27	F2 Execution
G - PEOPLE, CADRE AND CURRENCY						
G1	Submission	EXCON/Instructor/OT establishment requirement	The positions case to J1 for Div case establishment approval.	COMD PG/J7/COMD SBT	Oct-26	DG-2/CM1
G2	Policy	J7 Qualifications and currency Rules	The rules J7 owns as key client. J1 holds the record, J6 builds and hosts. J7 must not build parallel database	COMD J7	Q4-26	Stage 1, DG-2
G3	Specification	Qualification and currency system requirements to J6	The functional requirements J6 builds against, agreed with J1 as record owner	PG HQ	Sep-26	G2 execution
G4	Plan	OT and EXCON cadre generation and sustainment plan	How the cadre is recruited, trained, accredited, held current and rotated against the critical path	COMD J7	Q1-27	SG-2/CM1
G5	Plan	Overseas course pipeline plan	The managed pipeline developing SQEP among staff officers and specialist MOS. Interfaces with J1's MQC work	COMD J7	Q4-26	ST9
H - INTERNATIONAL ENGAGEMENT						
H1	Plan	J7 International Engagement Plan	Partner mapping, engagement priorities and the sequencing of activity toward combined participation in the 2030 MRE	COMD PG/J7	Q4-26	
H2	Directive	MCTM/USMC exploitation arrangement	Formalises access to Marine Corps Training, OT accreditation support and exercise design expertise	COMD PG/J7	Q1-27	DG-2
H3	Plan	Overseas Training Exercise Program Plan	The OTX design, partner allocation and delivery schedule	COMD J7	Q2-28	DG-5
H4	Directive	Releasability, Interoperability and scheduling arrangements	The coalition enablers secured ahead of combined activity in 2029	COMD PG/MOD	Q4-28	MRE
I - FACILITIES AND ESTATE						
I1	Terms of reference	SCIF and Exercise C2 accommodation and specialist Training facilities	The facilities case to J4/CMW/CFD/MOD	COMD J7/J4	Q4-26	DG-0, DG-3
I2	Directive	Hameem mission-rehearsal development case	The capital case to bring Hameem (and HAMRA and OMD 25) to MRE standard. Long lead time, cannot be recovered if started late	PG COMD/J7/J4	Q3-27	DG-6, MRE
I3	Submission	Training Area and population-centre access plan	Identifies and secures access to urban and population centre training opportunities through MOU	COMD J7	Q2-27	ST6
J - INSTRUMENTS J7 REQUIRES FROM OTHERS						
J1	Directive	ORC start date and cycle	J3 owned	COMD J3	Immediate	Everything
J2	Standard	Operational Performance Standards - one per SAG	J3 develops, J7 benchmarks against them. 21 required, priorities from COMD PG	COMD J3	Q4-26	C4, DG-2
J3	Directive	Written confirmation of the simulation direction	Converts COMD J3s verbal direction to citable authority	COMD J3	Immediate	LoE2
J4	Directive	SBT validation authority (certify/fail/remediate)	Requested at B3. Must precede the first SAG validation	PGHQ	Q4-27	Stage 5
J5	Directive	J7 as Collective training Requirements Authority	Requested at A6	PGHQ	Q4-26	Stage 3
J6	Directive	Formation and Manning of the three 1 star JTF HQs	J3 and Bdes responsibility.	COMD J3/BDEs	Q1-28	DG-5
J7	Approval	Divisional Establishment Approval	The annual approval submission at G1	J1/PGHQ	Dec-26	DG-2
J8	Schedule	Digital Spine, network and accreditation schedule	J6 delivery plan against E3, J7s largest external dependency apart from SBT	COMD J6	Q1-27	DG-6
J9	Directive	Reconciliation of SBTs for 19 DMTs against the 21 SAGs	Commanders direction required. Must settle before validation criteria are published	COMD PG	Q4-26	C4, B6
